

What is left to finish the website

The website, the registration and payment system, the database and the admin are **built and tested**. What is left is mostly things only you or Psoola can give, then putting everything on the real server and opening registration.

154 / 154

automatic checks pass

9

things needed from you

4

things needed from
Psoola

~25 Oct

target: registration
opens

The two things that block everything: (1) the **server and the domain**, and (2) **Psoola's documents and test keys**. Everything else can be done in parallel. Psoola usually takes the longest, so please send them the questions this week.

1 What is already done

- ✓ Website pages in English, Arabic and Kurdish, with the registration form, payment page and ticket page
- ✓ **Only people who pay are registered;** unpaid forms are deleted automatically
- ✓ Students upload their ID photo; it is **stored in the database** and shown in the admin (no approval step)
- ✓ Payment flow for Visa, MasterCard, FIB and FastPay (tested with a pretend Psoola)
- ✓ Exact amount only; paid twice = one ticket; fake payment messages refused
- ✓ PDF ticket with a signed QR code, and the ticket email in 3 languages
- ✓ Admin: Dashboard, Registrations, Lists, Payments, Workshops, Sponsors & booths, Check-in, Settings, Users
- ✓ Lists: lunch day 1 / day 2, students, student ID photos, workshops with their people, sponsors, exhibition booths (Excel + print)
- ✓ **Workshops in the database:** add, edit, seats +/-, hide; the website updates itself; seat limits enforced
- ✓ Workshop booking by phone, paid / not paid, exact amount, no refunds
- ✓ Phone registration with a "Pay now" link; free tickets by the Owner
- ✓ Event has no seat limit; lunch limits from the caterer
- ✓ Door check-in on a phone, with QR scanning
- ✓ Security: own accounts, 5 roles, phone codes, locks, audit log, private data protected
- ✓ Nightly database backup (including the ID photos); price-change alerts
- ✓ Tools to put it on the server (test site first, then live) and to upgrade the database safely
- ✓ Staff guide PDF (19 pages, with screenshots) and the earlier plan and Psoola documents

2 Final double-check (27 September)

Fresh copy from GitHub, empty database	Installed exactly as on the real server: 16 tables, 9 views, workshops, first Owner account. 154 of 154 automatic checks pass, twice in a row.
Real browser, 3 languages	Pay (English), student with ID photo (Arabic), declined payment (Kurdish), sponsor form, every admin page: no errors. All 6 pages load correctly in English, Arabic and Kurdish (right-to-left where needed) and fit a phone screen.

Every file	70 PHP, 38 JavaScript and all language files: no errors. Practice deploy to a pretend server: first install and update both work; the backend stays outside the public folder; nothing you edit in the admin is overwritten.
Independent review	Confirmed: nobody can be registered without a confirmed payment . It found 16 smaller problems, all fixed and covered by new checks: staff can no longer cancel a paid workshop or change workshop prices; a late second payment is never lost; a registered student's photo can never be deleted by the clean-up; the payment page text works on any server; full lunch has its own message; the Print button works; the daily totals now include money held for Finance; the phone layout of the Kurdish/Arabic registration page is fixed.

3 What I need from you

#	What	Why	When
1	Domain (ismile.krd suggested) and cPanel hosting with PHP 8.1+, MySQL, SSL, Cron Jobs, Terminal and Git. Share the login by phone, not in chat.	Nothing can go online without it.	now
2	Send the Psoola questions (the "Questions for Psoola" PDF on your Desktop) and ask for a merchant account.	Their answer is the longest wait.	this week
3	Ticket prices in IQD : professional, student, lunch day 1, lunch day 2.	Nobody can pay while a price is 0.	before opening
4	Lunch limits for day 1 and day 2 (from the caterer).	The lunch days close by themselves when full.	before opening
5	The workshops : names, trainers, prices and seats (you can add them yourself in the admin).	Shown on the website and booked by phone.	when known
6	The team : who is Owner, Finance, office (Registration), door staff (Check-in); who keeps the phone-code envelope.	Each person gets their own account.	before opening
7	A free Brevo account (brevo.com) for tickets@ismile.krd.	Sends the ticket emails; I add its records to the domain so emails do not go to spam.	with the server
8	Short answers : the office phone number for the bottom of emails, the workshop booking phone number, are age and gender still needed on the form, the opening date text.	These appear on the form, emails and website.	before opening
9	Someone to read the Kurdish and Arabic of the new texts (the "pay now" email, the "not completed" page) and the privacy notice I will write.	My translations should be checked by a native speaker.	before opening


4 What I need from Psoola

1	Merchant account, API documentation and test keys. I connect the 3 marked places in the code and test with their test keys (about 2 days).	critical
2	Register our payment-message (webhook) address: https://ismile.krd/api/webhook.php and the test one on test.ismile.krd.	Psoola
3	Their fee per payment , so it can be included in the ticket price.	Psoola
4	Whether they can refuse a second payment for the same reference (stops "paid twice" completely), and the live keys before opening.	Psoola

5 What I will do

#	Step	Needs	Time
1	Saved to GitHub (branch <i>backend</i>), done. On launch day it becomes the live website.	—	done
2	Set up the test site (test.ismile.krd): database, timed jobs, your Owner account; run the 154 checks on the real server; fix what only a real server shows (permissions, headers).	server + domain	1–2 days
3	Connect emails (Brevo) and the domain records; test that tickets arrive and do not go to spam.	Brevo account	half a day
4	Connect Psoola and test every case with their test keys: paid, declined, wrong amount, paid twice, lost message.	Psoola documents	about 2 days
5	Write the privacy notice (what we collect and why) in 3 languages, for your approval.	nothing	half a day
6	Check whether the hosting is behind Cloudflare (so the spam limits count each visitor), and final security check.	server	hours
7	Put the live site on ismile.krd; create the staff accounts; enter prices, workshops and lunch limits with you.	steps 2–4 done	1 day
8	Go-live check : one real small payment, ticket received, email test mode switched off, two-person sign-off. Then open registration .	live keys	1 day
9	Update the older backend PDFs (they still describe the student approval step that was removed).	nothing	hours

6 Timeline

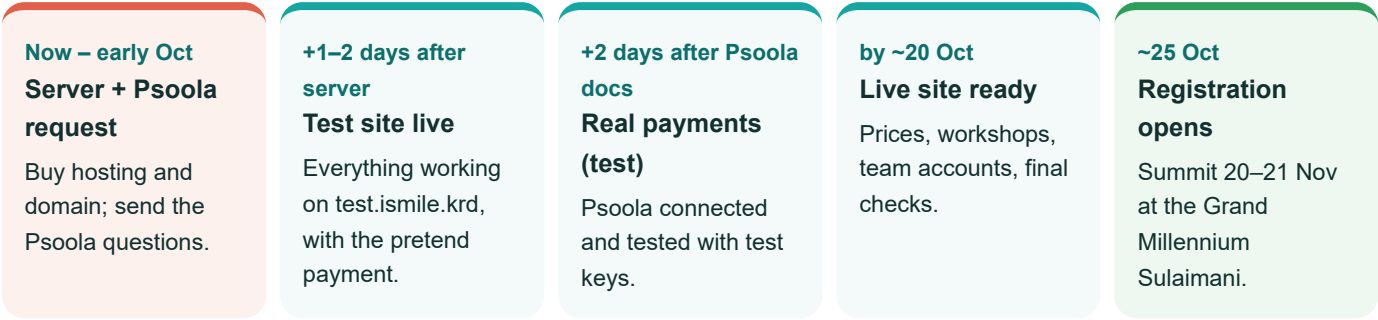

If Psoola's documents arrive after about 15 October, the opening date moves later by the same amount. Everything else can be ready and waiting.

7 Documents on your Desktop

iSmile 2026 - Admin guide for staff (how to use the database).pdf	How to use the admin, step by step with screenshots. Give it to the team.
iSmile 2026 - Questions for Psoola.pdf	Send this to Psoola.
iSmile 2026 - Backend Plan... and ...What I need from you and from Psoola.pdf	The original plan (some parts have since changed, see section 1).
iSmile 2026 - Backend, everything I built.pdf and ... Backend built (what I did and what I need).pdf	Earlier reports; they still mention student approval, which was removed. I will update them.
